

RAM INVESTMENT & CAPITAL PROJECTS MANAGEMENT PROCESS MANUAL

L0-2 Investment & Capital Projects Management

Value Stream: L0-2 Investment & Capital Projects Management

Process Owner: Chief Investment Officer

Governance Scope: L0, L1, and L2 Processes (Acquisition, Development, Construction, Divestment)

1. Process Purpose & Value Proposition

The purpose of the **L0-2 Investment & Capital Projects Management** Value Stream is to identify, evaluate, acquire, develop, enhance, and dispose of real estate assets while maximizing investment returns, ensuring governance compliance, and creating sustainable portfolio value.

Core Objectives:

- Identify and screen high-quality real estate investment opportunities aligned with the L0-1 Strategic Plan.
- Conduct rigorous feasibility, due diligence, and financial modeling to validate investment viability.
- Securely acquire and legally onboard assets through structured negotiation and transaction management.
- Plan, design, and deliver capital projects (new developments, major refurbishments) on time, within budget, and to safety/quality standards.
- Execute value-maximizing divestments and exits for assets that no longer fit the portfolio strategy.
- Ensure all processes comply with SAP workflows, regulatory requirements, and risk/ESG oversight.

2. High-Level Process Architecture (The 8-Step Capital Projects Methodology)

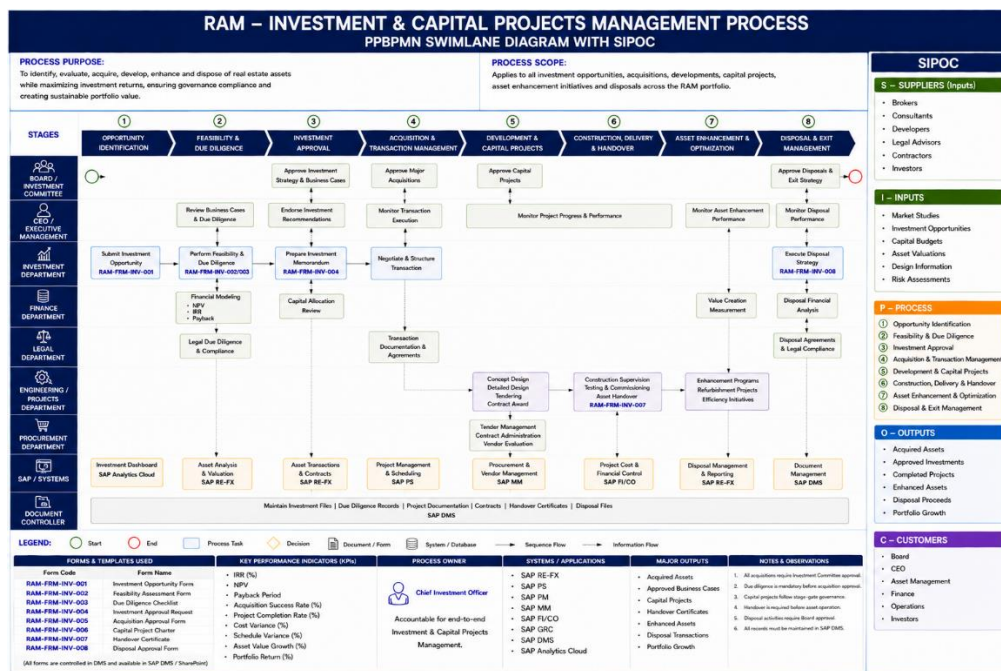


Figure 1: The 8-Step Capital Projects Methodology

Phase 1: Opportunity Identification

Purpose: To capture, screen, and prioritize real estate investment opportunities aligned with RAM's portfolio strategy.

- **Key Activities:** Market intelligence scanning, opportunity sourcing, preliminary screening (location, asset type, size), strategic fit assessment, and initial financial review.
- **Major Documents:** Market Intelligence Report (RAM-FRM-INV-001), Opportunity Capture Form (RAM-FRM-INV-002), Preliminary Financial Assessment (RAM-FRM-INV-004).

Phase 2: Feasibility & Due Diligence

Purpose: To evaluate the viability, returns, and strategic suitability of approved opportunities through comprehensive technical, financial, commercial, legal, and operational due diligence.

- **Key Activities:** Launch feasibility study, market/commercial analysis, technical/legal due diligence, financial modeling (NPV, IRR), risk assessment, and investment recommendation.
- **Major Documents:** Feasibility Study Initiation Form (RAM-FRM-INV-006), Market Assessment Report (RAM-FRM-INV-007), Legal Due Diligence Report (RAM-FRM-INV-008), Financial Feasibility Model (RAM-FRM-INV-009).

Phase 3: Investment Approval

Purpose: To secure formal governance approval for investments, allocate capital, and authorize acquisition execution.

- **Key Activities:** Investment submission, business case validation, financial risk review, Investment Committee review, capital allocation, and formal approval/communication.
- **Major Documents:** Investment Submission Form (RAM-FRM-INV-015), Investment Approval Request (RAM-FRM-INV-016), Risk & ESG Review (RAM-FRM-INV-017), Capital Allocation Form (RAM-FRM-INV-018).

Phase 4: Acquisition & Transaction Management

Purpose: To execute approved acquisitions through negotiation, contract preparation, transaction closing, ownership transfer, and asset onboarding.

- **Key Activities:** Transaction initiation, negotiation of commercial terms, structuring, legal documentation, approval of funding, financial closing, ownership transfer, and onboarding into portfolio.

- **Major Documents:** Acquisition Initiation Form (RAM-FRM-INV-022), Negotiation Summary Sheet (RAM-FRM-INV-023), Transaction Structure Assessment (RAM-FRM-INV-024), Financial Closing Certificate (RAM-FRM-INV-026).

Phase 5: Development & Capital Project Execution

Purpose: To plan, design, and deliver capital projects on time, within budget, and to quality/safety standards.

- **Key Activities:** Project initiation & planning, design & engineering, procurement/contracting, construction execution, monitoring & control, quality/safety compliance, and project closure.
- **Major Documents:** Project Initiation Form (RAM-FRM-INV-030), Project Charter (RAM-FRM-INV-031), Design & Engineering Report (RAM-FRM-INV-032), Contract Award Form (RAM-FRM-INV-033).

Phase 6: Asset Commissioning & Handover

Purpose: To ensure completed projects are tested, commissioned, and formally handed over to operations with all documentation, compliance, and asset information complete and accurate.

- **Key Activities:** Commissioning planning, systems/equipment testing, quality/compliance verification, documentation completion, operational readiness assessment, and asset registration.
- **Major Documents:** Commissioning Plan (RAM-FRM-INV-044), Commissioning Report (RAM-FRM-INV-045), Handover Certificate (RAM-FRM-INV-047), As-Built Documentation Checklist (RAM-FRM-INV-046).

Phase 7: Asset & Portfolio Management

Purpose: To optimize asset performance and portfolio value through proactive asset management, leasing, financial management, maintenance, risk management, and continuous portfolio monitoring.

- **Key Activities:** Portfolio planning, asset performance monitoring, leasing/revenue management, operations/maintenance, financial cost management, risk/compliance, and portfolio optimization.
- **Major Documents:** Asset Management Plan (RAM-FRM-INV-052), Leasing Strategy Form (RAM-FRM-INV-053), Maintenance & Operational Plan (RAM-FRM-INV-055), Portfolio Review & Optimization Report (RAM-FRM-INV-058).

Phase 8: Divestment & Exit Management

Purpose: To execute value-maximizing divestment and exit strategies for assets at the right time and under the right conditions to achieve investment objectives.

- **Key Activities:** Exit strategy planning, market/buyer assessment, preparation & valuation, marketing/outreach, negotiation, transaction documentation, financial closing, and post-exit review.
- **Major Documents:** Exit Strategy Planning Form (RAM-FRM-INV-059), Divestment Opportunity Assessment (RAM-FRM-INV-060), Buyer Due Diligence Checklist (RAM-FRM-INV-061), Divestment Exit Report (RAM-FRM-INV-065).

3. SIPOC Framework for L0-2 Investment & Capital Projects Management

S – Suppliers	I – Inputs	P – Process	O – Outputs	C – Customers
Board / Investment Committee CEO / Executive Mgmt. Asset Management Dept. Finance Department External Advisors (Legal, Brokers) Market Intelligence Providers	Market Studies Investment Opportunities Capital Budgets Asset Valuations Design Information Risk Assessments	Opportunity Identification Feasibility & Due Diligence Investment Approval Acquisition & Transaction Management Development & Capital Projects Construction & Handover Asset & Portfolio Management Divestment & Exit Management	Acquired Assets Approved Investments Completed Projects Enhanced Assets Divestment Proceeds Portfolio Growth	Board / Investment Committee CEO Asset Management Finance Operations Investors

4. Roles & Responsibilities

Role	Primary Responsibility in L0-2
Board / Investment Committee	Approves major acquisitions, project budgets, and divestment decisions over governance thresholds.
CEO / Executive Management	Provides strategic direction, approves major investments, and escalates critical project issues.
Chief Investment Officer (Process Owner)	Owner of the entire L0-2 Value Stream. Accountable for end-to-end investment, capital projects, asset management, and divestment processes.
Investment / Portfolio Strategy Team	Executes market scanning, financial modeling, due diligence, business case development, and deal structuring.
Engineering / Technical Team	Performs technical due diligence, manages design & engineering, and oversees construction quality.
Legal Department	Handles contract negotiation, legal documentation, ownership transfers, and regulatory compliance.
Finance Department	Manages funding availability, financial closing, cost control, and cash flow management on projects.
Risk / Compliance / ESG Team	Assesses project risks (market, operational, legal) and ensures ESG compliance and HSE oversight.
Procurement / Contracting Team	Manages the tendering, evaluation, and awarding of contracts for all capital projects.
Project Management Office (PMO)	Oversees project execution, monitors schedules/costs/quality, and manages project handover.

5. Key Performance Indicators (KPIs) & Success Metrics

The following KPIs are used to measure the health and success of the L0-2 Investment & Capital Projects Management process:

Financial & Strategic

- **Internal Rate of Return (IRR) (%)** – Core measure of investment profitability.
- **Net Present Value (NPV) (\$)** – Total value added by the project over its lifecycle.
- **Capital Expenditure Efficiency (%)** – Return on capital invested in projects.

- **Project Completion Rate (%)** – Percentage of projects completed on time and within scope.
- **Divestment Gain/Loss (%)** – Profit/loss realized from asset sales vs. book value.

Efficiency & Risk

- **Acquisition Conversion Rate (%)** – Percentage of screened opportunities that successfully close.
 - **Cost Variance (%)** – Percentage difference between actual project costs vs. approved budget.
 - **Schedule Performance Index (SPI)** – Ratio of earned value to planned value (schedule health).
 - **Due Diligence Accuracy Rate (%)** – Percentage of final financial models matching due diligence predictions.
 - **Post-Integration Compliance Score (%)** – Percentage of assets successfully onboarded into SAP RE-FX with 100% data accuracy.
 - **Risk Mitigation Completion (%)** – Percentage of identified project risks successfully mitigated.
-

6. Core Systems, Applications, and Data Flows

The L0-2 process relies heavily on the integration of the following systems:

System / Application	Function within L0-2
SAP Real Estate (RE-FX)	Central master data system for portfolio properties, asset onboarding, lease administration, and asset master records.
SAP Project System (PS)	Core system for capital project planning, WBS (Work Breakdown Structure), scheduling, and project cost tracking.
SAP Finance / FICO	Manages funding approval, budget allocation, cost settlements, and financial closings for acquisitions and projects.
SAP Plant Maintenance (PM)	Manages asset commissioning, maintenance plans, work orders, and operational handover documentation.
SAP Contract Management (SAP CLM / MM)	Manages procurement, tendering, contract awarding, supplier data, and contractor performance.
SAP GRC	Manages enterprise risk registers, compliance reviews, and ESG scoring for individual assets and projects.

System / Application	Function within L0-2
SAP DMS (Document Management)	Central storage for all L0-2 documents (RAM-FRM-INV forms, due diligence reports, legal contracts, as-built drawings).
SAP Analytics Cloud (SAC) / Power BI	Executive dashboards for project monitoring, portfolio health, KPI tracking, and scenario modeling.
SharePoint / Collaboration	Cross-functional collaboration hub for deal teams, project steering committees, and document reviews.

7. Data Governance & Administration Notes

To ensure integrity in the L0-2 process, the following data and document rules must be adhered to:

- Document Control:** All forms (RAM-FRM-INV-001 through ST-INV-065) are managed and stored in **SAP DMS** or **SharePoint** for full auditability.
- Retention Policy:** All acquisition documents, legal contracts, financial models, as-built drawings, and divestment reports must be retained in SAP DMS for a minimum of **7 years** to align with legal and corporate retention policies.
- Approval Thresholds:**
 - CapEx approvals** must follow the governance stage-gate process (Phase 3).
 - Contracts** exceeding \$X Million require Board approval; others can be approved by the CEO/CIO.
- Data Quality:**
 - Master Data:** All assets onboarded via Phase 4 must have 100% accurate property and legal data entered into **SAP RE-FX**.
 - Financials:** All project costs must be booked against the correct WBS in **SAP PS** within 24 hours of accrual.
- Confidentiality:** All due diligence reports, financial models, and transaction negotiation documents must be restricted to the Investment Committee, Legal, and the core deal team.

8. Key Governance & Exception Handling Rules (Common to all Phases)

In the case that an **investment fails the financial hurdle rate** (Phase 2), **cost overruns exceed 10% of budget** (Phase 5), or **legal/regulatory risks are deemed unacceptable** (Phase 2 & 7), the following escalation process applies:

1. **Redevelopment / Re-Negotiation Phase:** The Investment Team and Legal will document the root cause of the failure (e.g., "Zoning approval changed, increasing costs by \$X").
2. **Alternative Scenarios:** The team will run 2-3 alternative scenarios (e.g., reduce project scope, delay acquisition, renegotiate contractor pricing).
3. **Executive Steering Committee Review:** The CEO, CIO, and CFO will review the "Exception Case" in a special steering committee meeting to either **approve the alternative** or **terminate the initiative**.
4. **Formal Documentation:** A final "Project/Investment Disposition Log" is created in **SAP DMS** for historical audit purposes.

9. L0-2 KPI Data Dictionary (Definitions & Calculation Methods)

To ensure the manual is actionable, the following definitions must be used across all systems and reports. If these do not match SAP FICO/PS exactly, the SAP standards for finance/project metrics take precedence.

KPI Name	Definition	Formula / Calculation Method	Data Source	Target Frequency
Internal Rate of Return (IRR)	The annualized rate of growth that an investment is expected to generate.	Calculated via Excel/NPV function from Projected Cash Flows.	SAP FICO / Excel	Per Project
Net Present Value (NPV)	The difference between the present value of cash inflows and outflows over a period of time.	$\sum [(Net\ Cash\ Flow / (1 + Discount\ Rate)^{Year})] - Initial\ Investment.$	SAP FICO / Excel	Per Project
Capital Expenditure Efficiency	The percentage of actual capital expenditure that resulted in direct asset	$(Total\ NOI\ Increase\ attributable\ to\ CapEx / Total\ CapEx\ Spent) \times 100.$	SAP PS / SAP RE-FX	Per Project

KPI Name	Definition	Formula / Calculation Method	Data Source	Target Frequency
	value increase (e.g., new rentable area).			
Project Completion Rate (%)	Percentage of major capital projects completed on or before the approved original deadline.	$(\text{Number of Projects Completed on Time} / \text{Total Number of Projects Completed}) \times 100.$	SAP PS	Quarterly
Cost Variance (%)	Percentage difference between the actual cost spent on a project vs. the approved budget.	$[(\text{Actual Cost} - \text{Budgeted Cost}) / \text{Budgeted Cost}] \times 100.$	SAP PS / SAP FICO	Monthly
Schedule Performance Index (SPI)	A measure of project schedule efficiency.	$\text{Earned Value (EV)} / \text{Planned Value (PV)}.$	SAP PS	Monthly
Acquisition Conversion Rate (%)	The percentage of potential deals (opportunities) that result in a successfully closed asset.	$(\text{Number of Closed Acquisitions} / \text{Number of Total Opportunities Screened}) \times 100.$	SAP RE-FX / Opportunity Mgmt	Quarterly
Divestment Gain/Loss (%)	Profit or loss realized upon the sale of an asset.	$[(\text{Sale Price} - \text{Net Book Value}) / \text{Net Book Value}] \times 100.$	SAP FICO / SAP RE-FX	Per Divestment
Asset Onboarding Data Accuracy	Percentage of data fields in SAP RE-FX filled correctly within 7 days of closing.	$(\text{Fields with Correct Data} / \text{Total Required Data Fields}) \times 100.$	SAP RE-FX (Data Checks)	Per Acquisition

10. Execution Playbooks (Phase 1 to Phase 8)

Phase 1: Opportunity Identification Playbook

- **Primary Owner:** Chief Investment Officer (CIO)
- **Trigger:** Market shifts, availability of target assets, or strategic plan directives (Phase 1).
- **Key Workflow Steps:** Market Scanning → Opportunity Sourcing → Preliminary Screening → Strategic Fit Assessment → Initial Financial Review → Opportunity Prioritization → Pipeline Registration → Go/No-Go Decision.
- **Major Output:** A pipeline of vetted opportunities (RAM-FRM-INV-003) ready for Phase 2 due diligence.

Phase 2: Feasibility & Due Diligence Playbook

- **Primary Owner:** Investment Analyst / Legal / Engineering
- **Trigger:** A "Go" decision from Phase 1.
- **Key Workflow Steps:** Launch Feasibility Study → Market/Commercial Analysis → Technical Due Diligence → Legal/Regulatory Review → Financial & Risk Modeling → Consolidated Investment Assessment → Final Investment Recommendation.
- **Major Output:** A completed Financial Feasibility Model (RAM-FRM-INV-009) and Risk Assessment (RAM-FRM-INV-011) submitted for Phase 3 approval.

Phase 3: Investment Approval Playbook

- **Primary Owner:** Chief Investment Officer / Investment Committee
- **Trigger:** Completion of Phase 2 due diligence.
- **Key Workflow Steps:** Investment Submission → Business Case Validation → Financial & Risk Review → Committee Review → Governance Approvals → Capital Allocation → Final Investment Decision → Approval Communication.
- **Major Output:** Approved Investment Letter (RAM-FRM-INV-020) and Capital Allocation Form (RAM-FRM-INV-018).

Phase 4: Acquisition & Transaction Management Playbook

- **Primary Owner:** Investment Team / Legal Department
- **Trigger:** Formal Investment Approval (Phase 3).
- **Key Workflow Steps:** Transaction Initiation → Negotiation & Commercial Terms → Acquisition Structuring → Legal Documentation → Transaction Approvals → Financial Closing → Ownership Transfer → Asset Onboarding.
- **Major Output:** A fully executed Asset Master Record in SAP RE-FX and completed Acquisition Completion Report (RAM-FRM-INV-029).

Phase 5: Development & Capital Project Execution Playbook

- **Primary Owner:** Project Management Office (PMO) / Construction Team
- **Trigger:** Project handover from Acquisition team (or internal strategic directive for new developments).

- **Key Workflow Steps:** Project Initiation & Planning → Design & Engineering → Procurement & Contracting → Construction Execution → Monitoring & Control → Quality, Safety & Compliance → Commissioning & Handover → Project Closure.
- **Major Output:** Completed construction, signed Handover Certificate (RAM-FRM-INV-041), and Project Closure Report (RAM-FRM-INV-043).

Phase 6: Asset Commissioning & Handover Playbook

- **Primary Owner:** Project Manager / Operations Team
- **Trigger:** Completion of Phase 5 construction.
- **Key Workflow Steps:** Commissioning Planning → Systems & Equipment Testing → Quality & Compliance Verification → Documentation Completion → Operational Readiness Assessment → Final Handover Approval → Asset Registration & Activation → Post-Handover Review.
- **Major Output:** Handover Certificate (RAM-FRM-INV-047), Asset Activation in SAP PM, and Post-Handover Review (RAM-FRM-INV-048).

Phase 7: Asset & Portfolio Management Playbook

- **Primary Owner:** Asset Management & Finance Teams
- **Trigger:** Ongoing operational phase of the asset lifecycle.
- **Key Workflow Steps:** Portfolio Planning → Asset Performance Monitoring → Leasing & Revenue Management → Operations & Maintenance → Financial & Cost Management → Risk & Compliance Management → Portfolio Review & Optimization → Reporting & Communication.
- **Major Output:** Optimized Portfolio Dashboard, Asset Performance Index (API), and Portfolio Review & Optimization Report (RAM-FRM-INV-058).

Phase 8: Divestment & Exit Management Playbook

- **Primary Owner:** Investment Team / Legal / Finance
 - **Trigger:** Strategic directive to dispose of an asset based on L0-1 portfolio strategy or Phase 7 performance reviews.
 - **Key Workflow Steps:** Exit Strategy Planning → Market & Buyer Assessment → Preparation & Valuation → Marketing & Investor Outreach → Negotiation & Due Diligence → Transaction Documentation → Closing & Fund Realization → Post-Exit Review & Reporting.
 - **Major Output:** Completed Transaction, Final Investment Returns, Divestment Exit Report (RAM-FRM-INV-065).
-

11. Standard Operating Procedure (SOP) – Monthly Project & Portfolio Performance Review Meeting

SOP Number: RAM-L0-2-SOP-001

Frequency: Monthly (Second Wednesday of each month)

Duration: 90 Minutes

Chair: Chief Investment Officer (CIO)

Attendees: Head of PMO, Head of Finance, Head of Legal, Head of Asset Management, Project Managers.

Meeting Agenda & Flow:

Time	Agenda Item	Owner	Action Expected
0-15 mins	Active Deal Pipeline Review: Quick status check on opportunities in Phases 1 & 2 (Pipeline health).	Investment Director	Determine if any deals need resource acceleration.
15-45 mins	Project Status Deep Dive: Review of Top 5 active Capital Projects (Phase 5). Focus on: Cost Variance, Schedule Variance, and Major Risks.	PMO / Project Manager	Approve budget variances or escalate to Steering Committee.
45-60 mins	Completed Project Handover Reviews: Check status of assets in Phase 6 (Commissioning). Ensure operational readiness is on track.	Operations / PM	Approve final handover certificates.
60-80 mins	Asset Performance & Divestment Check: Review underperforming assets (from Phase 7) and divestment pipeline (Phase 8).	Asset Management / Finance	Approve initiating Phase 8 for identified assets.
80-90 mins	Action Items & Next Steps: Formalize decisions, assign owners, update the Action Tracker (RAM-FRM-INV-064).	CIO	Ensure decisions are logged in SAP DMS.

Outputs: Meeting minutes documented and stored in SAP DMS; Action Tracker updated; Approved budget re-allocations pushed into SAP FICO/PS.

12. Full Template Library (RAM-FRM-INV-001 to 065)

(Note: To save space, I will provide the 10 most critical templates as detailed examples, ensuring your team has the core to build the rest upon.)

FORM INV-001: Market Intelligence Report (Phase 1)

- **Sections:** Market Data Collection (Macro, Competitive), Market Analysis (Sector Trends), Acquisition Leads, Investment Opportunities Log.
- **Purpose:** To feed the Opportunity Identification pipeline with live market data.

FORM INV-004: Preliminary Financial Assessment (Phase 1)

- **Sections:** Asset/Location Overview, Preliminary Revenue, Preliminary Cost/CapEx Estimate, Rough ROI/IRR Estimate, Go/No-Go Criteria Check.
- **Purpose:** To quickly filter out unviable deals before heavy due diligence spending.

FORM INV-009: Financial Feasibility Model (Phase 2)

- **Sections:** Capital Expenditure Budget, Tenant Revenue Projections, Operating Expense Forecasts, Cash Flow Statement, DCF/NPV/IRR Calculation, Funding Requirements.
- **Purpose:** To provide the rigorous financial backing for investment approval.

FORM INV-016: Investment Approval Request (Phase 3)

- **Sections:** Project Summary, Strategic Alignment (from L0-1), Capital Request (\$), Risk/ESG Compliance Checklist, Financial Summary, Schedule.
- **Purpose:** The formal document submitted to the Investment Committee.

FORM INV-024: Transaction Structure Assessment (Phase 4)

- **Sections:** Deal Structure (SPV/JV/Asset Purchase), Tax Considerations (Pre/post-tax impact), Financing Structure (Debt/Equity split), Legal Entity to acquire, Exit mechanism.
- **Purpose:** To legally and financially structure the acquisition before signing.

FORM INV-031: Project Charter (Phase 5)

- **Sections:** Project Name/ID, Project Manager, Executive Sponsor, Scope Statement, High-Level Budget, High-Level Schedule, Resource Requirements, Key Stakeholders.

- **Purpose:** The foundational document that authorizes the capital project to move into design/execution.

FORM INV-033: Contract Award Form (Phase 5)

- **Sections:** Tender Reference, Bidders Evaluated, Winning Vendor, Contract Value, Scope of Work, Contract Start/End Dates, Payment Terms.
- **Purpose:** To formally document the procurement decision and award the contract to the chosen vendor.

FORM INV-046: As-Built Documentation Checklist (Phase 6)

- **Sections:** Mechanical Drawings, Electrical Schematics, Architectural Plans, Asset Tagging, O&M Manuals, Warranties, Spare Parts Inventory.
- **Purpose:** To ensure all technical documentation is handed over to operations.

FORM INV-059: Exit Strategy Planning Form (Phase 8)

- **Sections:** Asset ID, Reason for Exit (Performance vs. Strategy), Target Timeline, Expected Divestment Price, Preferred Buyer Type, Tax/Legal Implications, Exit Team.
- **Purpose:** The initial planning document for beginning the divestment process.

FORM INV-064: Action Tracker & Implementation Log (All Phases)

- **Sections:** Action Item ID, Project Reference, Action Description, Assigned Owner, Priority (H/M/L), Due Date, Status, Notes/Comments.
- **Purpose:** To track all decisions, tasks, and corrections identified in monthly reviews.

Summary: L0-2 Full Reconciliation Checklist

Uploaded Image #	Phase/Title	Covered in Manual?
1	L0-2 Overall Value Stream & SIPOC	✓ Yes (Section 1, 2, 3, 8)
2	Phase 1: Opportunity Identification	✓ Yes (Playbook & Templates)
3	Phase 2: Feasibility & Due Diligence	✓ Yes (Playbook & Templates)
4	Phase 3: Investment Approval	✓ Yes (Playbook & Templates)
5	Phase 4: Acquisition & Transaction	✓ Yes (Playbook & Templates)

L0-2 Investment & Capital Projects Management

6	Phase 5: Development & Project Execution	☒ Yes (Playbook & Templates)
7	Phase 6: Commissioning & Handover	☒ Yes (Playbook & Templates)
8	Phase 7: Asset & Portfolio Management	☒ Yes (Playbook & Templates)
9	Phase 8: Divestment & Exit	☒ Yes (Playbook & Templates)

L0-2 INVESTMENT & CAPITAL PROJECTS FORM TEMPLATES

1. FORM INV-001: MARKET INTELLIGENCE REPORT (Phase 1)

Purpose: To centralize all market data, trends, and new leads for the quarterly strategic pipeline review.

Field	Data Entry / Instructions
Report ID	[INV-001-YYYY-QX]
Reporting Period	[e.g., Q1 2026]
Prepared By	[Analyst Name]
Sector Focus (Check all that apply)	[] Office [] Retail [] Industrial [] Residential [] Hospitality
1. Macroeconomic Drivers	Interest Rate Trend: [Rising / Stable / Falling] Inflation Rate: [X]% GDP Growth Forecast: [X]% Construction Cost Index: [Trend]
2. Competitive Landscape	Major Deals Closed (Competitors): [List recent high-value acquisitions by Blackstone, Brookfield, local REITs, etc.] Pricing Trends (\$/Sqft): [Average asking rents in target submarkets]
3. New Investment Opportunities	Lead 1: [Property Name, Location, Size, Estimated Price, Seller] Lead 2: [Property Name, Location, Size, Estimated Price, Seller] Lead 3: [Property Name, Location, Size, Estimated Price, Seller]
4. Preliminary Opportunity Ranking	Priority 1 (High): [Lead Name] - aligns with Strategic Plan Goal X. Priority 2 (Medium): [Lead Name] - speculative, requires further research. Priority 3 (Low): [Lead Name] - does not align with current portfolio.

Field	Data Entry / Instructions
Sign-off (CIO)	(Date: //)

2. FORM INV-004: PRELIMINARY FINANCIAL ASSESSMENT (Phase 1)

Purpose: A "quick filter" to kill unviable deals *before* spending money on external due diligence.

Field	Data Entry
Opportunity Name	[e.g., XYZ Logistics Warehouse]
Location	[City, State]
Asset Class	[Office / Retail / Industrial / Residential]
Asking Price (\$)	\$ [Enter Amount]
Estimated Acquisition Costs (\$)	\$ [Enter Amount (Legal, surveys, etc.)]
Estimated CapEx (Initial)	\$ [Enter Amount for immediate repairs/refurb]
Total Initial Cash Required (\$)	\$ [Sum of above three fields]
Projected Gross Rent (\$/yr)	\$ [Enter expected annual rent]
Estimated OpEx (\$/yr)	\$ [Property taxes, insurance, utilities, mgmt fees]
Projected NOI (\$)	\$ [Gross Rent minus OpEx]
Initial Cap Rate (%)	[NOI ÷ Asking Price] %
Strategic Fit Check	[Does this asset align with L0-1 Strategic Plan? Yes / No]
Initial Risk Assessment	[Low / Medium / High] (e.g., "High risk: 50% vacancy forecast")
Recommendation	[] Proceed to Phase 2 Due Diligence [] Reject / Do not proceed

3. FORM INV-009: FINANCIAL FEASIBILITY MODEL (Phase 2)

Purpose: The comprehensive financial "heart" of the business case. This form is usually linked to an Excel model with formulas.

Category	Year 0 (Pre-Acquisition)	Year 1	Year 2	Year 3	Year 4	Year 5 (Exit)
1. Inflows (Revenue)						
Gross Rental Revenue	\$ -	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]
Other Income (Parking, etc.)	\$ -	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]
Total Revenue	\$ -	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]
2. Outflows (OpEx)						
Property Taxes	\$ -	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]
Insurance	\$ -	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]
Utilities / Maintenance	\$ -	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]
Mgmt Fees (% of rent)	\$ -	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]
Total OpEx	\$ -	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]
3. Net Operating Income (NOI)	\$ -	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]
4. Capital Expenditures	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ -
5. Debt Service (Interest+Principal)	\$ -	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]
6. Cash Flow After Debt	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]

7. Exit Sale Proceeds (Year 5)						\$ [X]
8. Net Cash Flow	(\$ [X])	\$ [X]	\$ [X]	\$ [X]	\$ [X]	\$ [X]
Final Metrics	Projected IRR: [X]%	Projected NPV: \$ [X]	Payback Period: [X] Years	Cap Rate on Exit: [X]%		

4. FORM INV-016: INVESTMENT APPROVAL REQUEST (Phase 3)

Purpose: The official "packet" submitted to the Investment Committee for an up/down vote.

Section	Details
1. Executive Summary	Project Name: [XYZ Logistics Center] Strategic Goal Alignment: [e.g., Goal 1: Increase GAV by expanding into industrial sector] Total Capital Request: \$ [X] Million Primary Financial Goal: [e.g., Achieve an IRR of 12% and an exit cap rate of 6.0%]
2. Financial Highlights	Total Investment: [X]M <i>< br > ** Equity/DebtSplit:**</i> [X] [X] Projected IRR (Base Case): [X]% Projected NPV (Base Case): \$ [X] M
3. Risk & ESG Checklist	Risk Level: [Low / Medium / High] Top Risk 1: [Description] - [Mitigation Plan] Top Risk 2: [Description] - [Mitigation Plan] ESG Certification Potential: [e.g., LEED Silver potential] Does this project violate any compliance/governance rules? [Yes / No]
4. Recommended Action	[] Approve (Proceed to Phase 4 Acquisition) [] Approve with Conditions (List conditions: _____) [] Reject

5. Investment Committee Vote	Chairperson Signature: _____ Date: // __ Outcome: Approved / Rejected / Tabled for Revisions
SAP Workflow Reference	[SAP Workflow Tracking ID assigned by SAP GRC]

5. FORM INV-024: TRANSACTION STRUCTURE ASSESSMENT (Phase 4)

Purpose: Legal and financial setup document before signing any binding agreements.

Field	Data Entry
Acquisition Legal Entity	[e.g., RAM Holdings SPV 01, LLC]
Transaction Type	[] Asset Purchase [] Share Purchase [] Joint Venture (JV) [] Leasehold Acquisition
Debt Financing Provider	[Bank Name]
Loan-to-Value (LTV) Ratio	[X]%
Interest Rate / Term	[X]% fixed for [X] years
Equity Partners / Structure	[If JV: RAM Equity [X]%, Partner Equity [X]%
Critical Closing Conditions	Condition 1: [e.g., Successful environmental Phase I completion.] Condition 2: [e.g., Receipt of local zoning permits.]
Tax Implications	[e.g., Standard transfer taxes of X% apply. No STCA liability.]
Required Legal Documents	[] Purchase Agreement [] Non-Disclosure Agreement (NDA) [] Title / Deed Search [] Zoning / Regulatory Compliance Certificates

6. FORM INV-031: PROJECT CHARTER (Phase 5)

Purpose: The foundational document that officially starts a capital construction/development project.

Field	Data Entry
Project Name	[e.g., Asset X Major Refurbishment]
Project ID	[SAP PS WBS Element: RAM-X-XXXX]
Project Manager	[Name]
Executive Sponsor	[Name (CIO/CEO)]
Project Scope (High-Level)	[Describe major work: e.g., Gut renovation of 50,000 sqft of office space, new HVAC installation, lobby modernization.]
Exclusions / Out of Scope	[List what is NOT included in this project.]
Approved Budget (\$)	\$ [X] Million
Projected Start Date	[DD/MM/YYYY]
Projected End Date	[DD/MM/YYYY]
Milestones	M1: Design & Permits Complete - [Date] M2: Tender Awarded - [Date] M3: Construction Start - [Date] M4: Substantial Completion - [Date]
Key Stakeholders	[Name: Role] (e.g., Asset Management, Finance, Operations, Leasing).
Key Risks (at Initiation)	Risk 1: [e.g., Supply chain delays for HVAC] - Mitigation: [e.g., Pre-order critical items 6 months early].
Approvals	CIO Signature: _____ Date: //

7. FORM INV-033: CONTRACT AWARD FORM (Phase 5)

Purpose: To formally document the procurement process and award the contract to the selected vendor.

Field	Data Entry
Tender Reference #	[Tender-2026-001]
Project Name	[Project Name from INV-031]
Contract Scope Summary	[e.g., Supply and install HVAC system for Asset X.]
Vendor Selection Summary	
Vendor A (Shortlisted)	[Name] - Bid: \$[X] - Score: [X]/100
Vendor B (Shortlisted)	[Name] - Bid: \$[X] - Score: [X]/100

Vendor C (Shortlisted)	[Name] - Bid: \$[X] - Score: [X]/100
Reason for Selection	[e.g., Best technical fit, most competitive pricing, local safety record.]
Awarded Vendor Details	Vendor Name: [Contractor Name] Contract Value: [X] <i>< br > ** PaymentTerms:**</i> [e. g., 15X million required.]
Award Approval	PMO Director: _____ Finance Controller: _____ Date: //

8. FORM INV-046: AS-BUILT DOCUMENTATION CHECKLIST (Phase 6)

Purpose: Used to hand over technical documentation and warranties to the Operations / Facility Management team.

Checklist Item	Status (Check when completed)	Comments/Location of File
1. Architectural As-Built Drawings	[] Completed	[SAP DMS Path]
2. Structural As-Built Drawings	[] Completed	[SAP DMS Path]
3. Mechanical (HVAC/Plumbing) Drawings	[] Completed	[SAP DMS Path]
4. Electrical Diagrams & Schematics	[] Completed	[SAP DMS Path]
5. O&M Manuals (All Major Systems)	[] Completed	[SAP DMS Path]
6. Equipment Warranties & Certificates	[] Completed	[SAP DMS Path]
7. Asset Register / Equipment Tags	[] Completed (Uploaded to SAP PM)	[SAP PM Plant Code]
8. Spare Parts List & Inventory	[] Completed	[Maintenance Office]

L0-2 Investment & Capital Projects Management

Checklist Item	Status (Check when completed)	Comments/Location of File
9. Fire Safety & Life Safety Certificates	[] Completed	[SAP DMS Path]
10. Commissioning Test Reports	[] Completed	[SAP DMS Path]
Handover Acceptance	Facilities Manager: _____ Project Manager: _____ Date: //	

9. FORM INV-059: EXIT STRATEGY PLANNING FORM (Phase 8)

Purpose: The kickoff document to initiate the divestment of an asset.

Field	Data Entry
Asset Name / ID	[Asset Name / SAP RE-FX ID]
Reason for Exit (Check primary reason)	☐ Non-core asset (Strategic mismatch) ☐ Underperforming asset (Low yield) ☐ End of lifecycle / High CapEx needed ☐ Capital recycling (Need funds for higher-yield opportunity)
Target Sale Price (\$)	\$ [X] Million
Estimated Net Book Value (\$)	\$ [X] Million
Target Profit / Gain (\$)	\$ [X] Million
Preferred Exit Timeline	[Q1 2026 / Q2 2026, etc.]
Preferred Buyer Profile	☐ Institutional Investor (REITs) ☐ Private Equity ☐ Owner-User ☐ Foreign Investor
Key Legal/Tax Restrictions	[e.g., "Asset must be held for 3 years to avoid STCA penalties. Sale will incur X% transfer tax."]
Required Due Diligence (Buyer's side)	☐ Updated Appraisal ☐ Condition Survey ☐ Environmental Report (Phase I) ☐ Rent Roll & Lease Abstracts
Approved by (CIO)	_____ Date: //

10. FORM INV-064: ACTION TRACKER & IMPLEMENTATION LOG (All Phases)

Purpose: The "living" master log used in every monthly L0-2 meeting to track tasks, issues, and decisions.

Action ID	Project/Phase Reference	Action Description	Assigned Owner	Priority (H/M/L)	Due Date	Status	Notes/Comments
ACT-001	Phase 2: XYZ Logistics	Complete geotechnical survey for the foundation.	[Engineering Team]	H	15/06/2026	In Progress	Awaiting weather clearance for drilling.
ACT-002	Phase 3: ABC Office Tower	Get final Insurance Certificate for debt financing.	[Legal / Finance]	H	01/06/2026	Not Started	Waiting on bank's final conditions.
ACT-003	Phase 5: Asset X Refurb	Order high-efficiency chillers (Lead time 14 weeks).	[PMO / Procurement]	M	10/06/2026	Completed	Purchase order sent to vendor.
ACT-004	Phase 8: Divestment Y	Prepare the marketing book for potential buyers.	[Investment Team]	M	30/07/2026	In Progress	Drafting market teaser sheet.
Closure Rules	An Action Item is considered "Closed" only when the task is fully completed and the associated SAP workflow						

L0-2 Investment & Capital Projects Management

Action ID	Project/Phase Reference	Action Description	Assigned Owner	Priority (H/M/L)	Due Date	Status	Notes/Comments
	<i>or document is updated and signed off.</i>						

How to deploy these forms in SAP/SharePoint environment:

1. **Word Version:** Copy the tables into Microsoft Word, ensure "Repeat header rows" is checked for the forms that span multiple pages (like INV-009 and INV-064), and save them as Master_Template.docx.
2. **Excel Version:** Copy the financial table in **INV-009** into Excel. Link the cash flow formulas (NOI, IRR, NPV) to Excel's built-in financial functions (=NPV(), =IRR()), so the model automatically calculates as soon as you type in the assumptions.
3. **SAP DMS Governance:** Upload these 10 Master Templates to your **SAP DMS** folder labeled RAM_L0-2_Master_Templates. When an analyst needs to use one, they must "Save As" a new file with the unique project ID (e.g., RAM-FRM-INV-016_XYZ_Logistics.docx). The original master files must be set to "Read-Only" for general users to prevent accidental overwrites.
