

L0-2- RAM INVESTMENT & CAPITAL PROJECTS MANAGEMENT PROCESS MANUAL

SQUAD CONSULTING

RAM – INVESTMENT & CAPITAL PROJECTS MANAGEMENT PROCESS

- Notes

PROCESS PURPOSE:

To identify, evaluate, acquire, develop, enhance and dispose of real estate assets while maximizing investment returns, ensuring governance compliance and creating sustainable portfolio value.

PROCESS SCOPE:

Applies to all investment opportunities, acquisitions, developments, capital projects, asset enhancement initiatives and disposals across the RAM portfolio.

SIPOC

S – SUPPLIERS (Inputs)

- Brokers
- Consultants
- Developers
- Legal Advisors
- Contractors
- Investors

I – INPUTS

- Market Studies
- Investment Opportunities
- Capital Budgets
- Asset Valuations
- Design Information
- Risk Assessments

P – PROCESS


- ① Opportunity Identification
- ② Feasibility & Due Diligence
- ③ Investment Approval
- ④ Acquisition & Transaction Management
- ⑤ Development & Capital Projects
- ⑥ Construction, Delivery & Handover
- ⑦ Asset Enhancement & Optimization
- ⑧ Disposal & Exit Management

0 – OUTPUTS

- Acquired Assets
- Approved Investments
- Completed Projects
- Enhanced Assets
- Disposal Proceeds
- Portfolio Growth

C – CUSTOMERS

- Board
- CEO
- Asset Management
- Finance
- Operations
- Investors

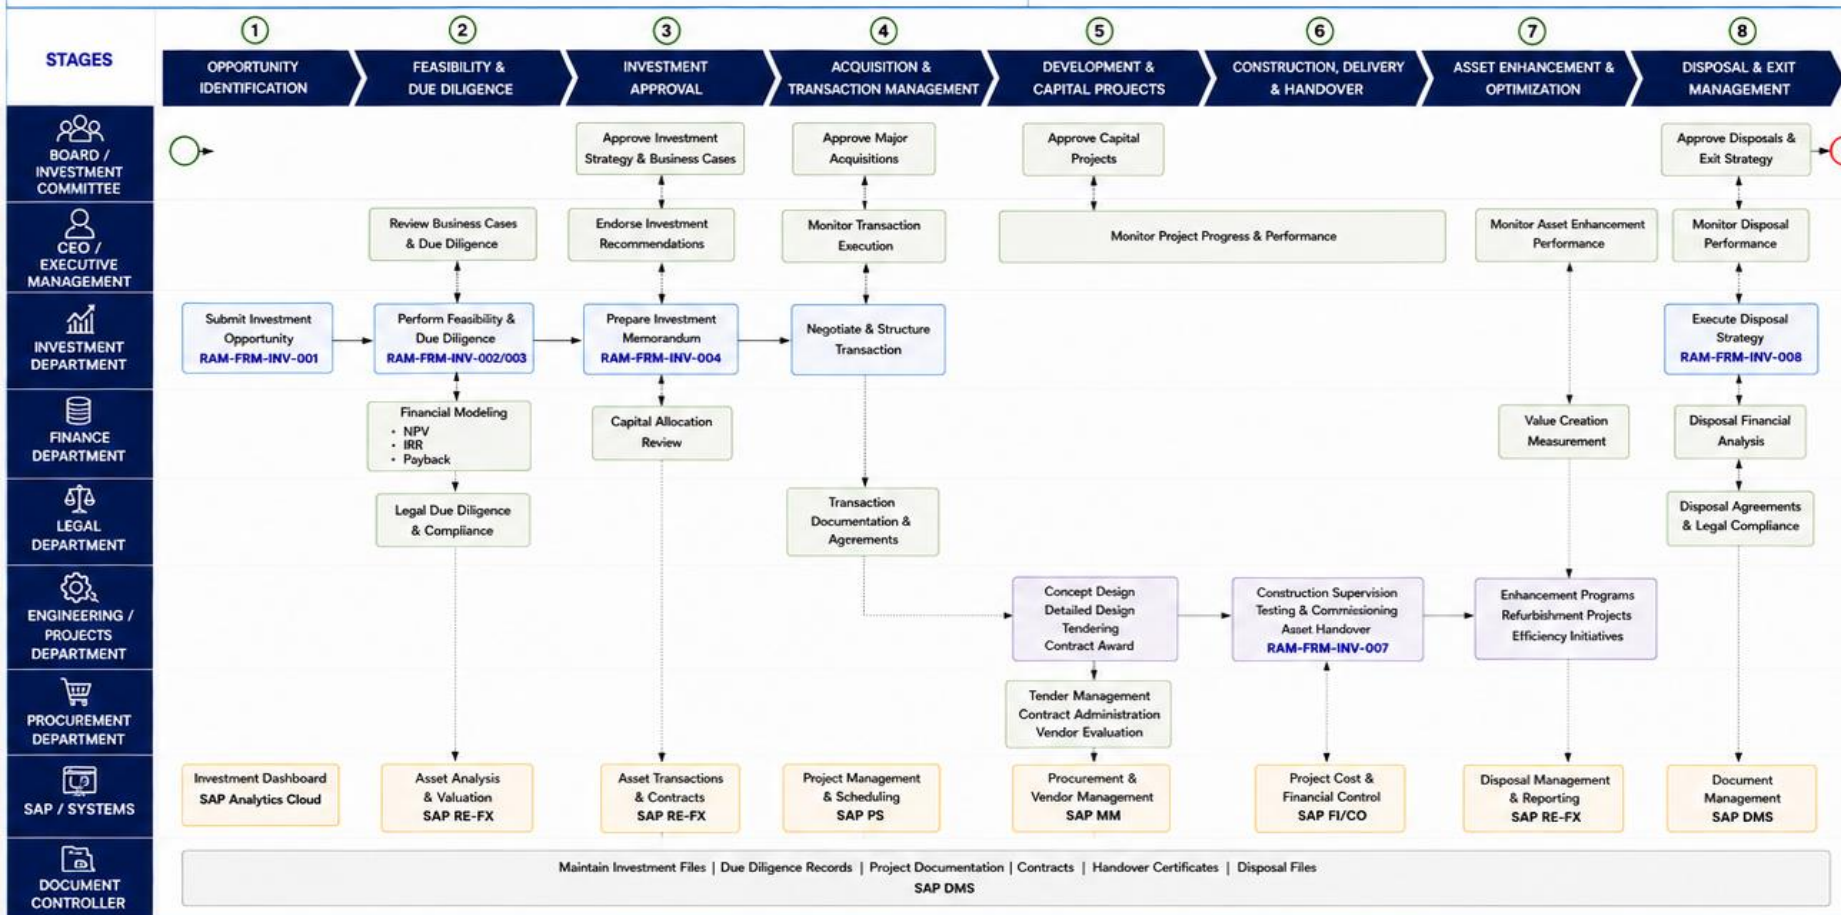

LEGEND: ○ Start ○ End □ Process Task ◇ Decision 📄 Document / Form 🗄 System / Database → Sequence Flow Information Flow

FORMS & TEMPLATES USED		KEY PERFORMANCE INDICATORS (KPIs)	PROCESS OWNER	SYSTEMS / APPLICATIONS	MAJOR OUTPUTS	NOTES & OBSERVATIONS
Form Code	Form Name	- IRR (%) - NPV - Payback Period - Acquisition Success Rate (%) - Project Completion Rate (%) - Cost Variance (%) - Schedule Variance (%) - Asset Value Growth (%) - Portfolio Return (%)	 Chief Investment Officer Accountable for end-to-end Investment & Capital Projects Management.	- SAP RE-FX - SAP PS - SAP PM - SAP MM - SAP FI/CO - SAP GRC - SAP DMS - SAP Analytics Cloud	- Acquired Assets - Approved Business Cases - Capital Projects - Handover Certificates - Enhanced Assets - Disposal Transactions - Portfolio Growth	- All acquisitions require Investment Committee approval. - Due diligence is mandatory before acquisition approval. - Capital projects follow stage-gate governance. - Handover is required before asset operation. - Disposal activities require Board approval. - All records must be maintained in SAP DMS.
(All forms are controlled in DMS and available in SAP DMS / SharePoint)						

RAM – INVESTMENT & CAPITAL PROJECTS MANAGEMENT PROCESS

PHASE 1 – OPPORTUNITY IDENTIFICATION

PPBPMN SWIMLANE DIAGRAM WITH SIPOC

PROCESS PURPOSE:

To identify, capture, screen and prioritize real estate investment opportunities aligned with RAM portfolio strategy and growth objectives.

PROCESS SCOPE:

Applies to all acquisition opportunities, development opportunities, joint ventures, strategic investments and asset acquisition proposals entering the investment pipeline.

STAGES

BROKERS /
MARKET SOURCES

INVESTMENT
ANALYST

PORTFOLIO &
STRATEGY TEAM

FINANCE
DEPARTMENT

RISK
MANAGEMENT

CHIEF
INVESTMENT OFFICER

SAP / SYSTEMS

DOCUMENT
CONTROLLER

LEGEND: Start End Process Task Decision Document / Form System / Database Sequence Flow Information Flow

FORMS & TEMPLATES USED (This Phase)

Form Code	Form Name
RAM-FRM-INV-001	Market Intelligence Report
RAM-FRM-INV-002	Opportunity Capture Form
RAM-FRM-INV-003	Initial Screening Checklist
RAM-FRM-INV-004	Preliminary Financial Assessment
RAM-FRM-INV-005	Go / No-Go Decision Form

(All forms are controlled in DMS and available in SAP DMS / SharePoint)

KEY PERFORMANCE INDICATORS (KPIs)

- Opportunities Identified (#)
- Screening Success Rate (%)
- Opportunity Conversion Rate (%)
- Average Screening Cycle Time (Days)
- Investment Pipeline Value
- Strategic Fit Score

PROCESS OWNER



Chief Investment Officer

Accountable for opportunity sourcing and investment pipeline development.

SYSTEMS / APPLICATIONS

- SAP RE-FX
- SAP Analytics Cloud
- CRM
- SAP DMS
- Power BI

NOTES / OBSERVATIONS

1. All opportunities shall be screened before entering the pipeline.
2. Strategic alignment is mandatory before feasibility studies.
3. Initial financial review is indicative only.
4. Opportunities rejected at this stage shall be archived.
5. Approved opportunities proceed to Phase 2 – Feasibility & Due Diligence.
6. All records shall be maintained in SAP DMS.

SIPOC

S – SUPPLIERS (Inputs)

- Brokers
- Developers
- Consultants
- Market Research Firms
- Investment Banks
- Property Owners

I – INPUTS

- Market Reports
- Property Listings
- Opportunity Leads
- Economic Data
- Strategic Plan
- Portfolio Objectives

P – PROCESS

- ① Market Intelligence & Scanning
- ② Opportunity Sourcing
- ③ Preliminary Screening
- ④ Strategic Fit Assessment
- ⑤ Initial Financial Review
- ⑥ Opportunity Prioritization
- ⑦ Pipeline Registration
- ⑧ Go / No-Go Decision

O – OUTPUTS

- Opportunity Register
- Investment Pipeline
- Initial Financial Assessment
- Priority Ranking
- Approved Opportunities
- Rejected Opportunities

C – CUSTOMERS

- Investment Committee
- CEO
- Portfolio Management
- Asset Management
- Finance

RAM – INVESTMENT & CAPITAL PROJECTS MANAGEMENT PROCESS

PHASE 2 – FEASIBILITY & DUE DILIGENCE

PPBPMN SWIMLANE DIAGRAM WITH SIPOC

PROCESS PURPOSE:

To evaluate the viability, risks, returns and strategic suitability of approved investment opportunities through comprehensive technical, financial, commercial, legal and operational due diligence.

PROCESS SCOPE:

Applies to all investment opportunities approved in Phase 1 and covers feasibility studies, technical assessments, financial modelling, legal due diligence, market analysis and investment recommendation preparation.

SIPOC

S – SUPPLIERS (Inputs)

- Investment Department
- Market Research Firms
- Engineering Consultants
- Legal Advisors
- Valuation Experts
- Risk Management Team

I – INPUTS

- Approved Opportunity
- Market Data
- Site Information
- Financial Assumptions
- Legal Documents
- Regulatory Information

P – PROCESS

- ① Initiate Feasibility Study
- ② Market & Commercial Analysis
- ③ Technical Due Diligence
- ④ Legal & Regulatory Review
- ⑤ Financial Feasibility Analysis
- ⑥ Risk Assessment
- ⑦ Consolidated Investment Review
- ⑧ Investment Recommendation

O – OUTPUTS

- Feasibility Study
- Technical Due Diligence Report
- Legal Due Diligence Report
- Financial Model
- Risk Assessment Report
- Investment Recommendation

C – CUSTOMERS

- Investment Committee
- CEO
- Board
- Asset Management
- Finance Department

STAGES

①

②

③

④

⑤

⑥

⑦

⑧

INITIATE FEASIBILITY STUDY

MARKET & COMMERCIAL ANALYSIS

TECHNICAL DUE DILIGENCE

LEGAL & REGULATORY REVIEW

FINANCIAL FEASIBILITY ANALYSIS

RISK ASSESSMENT

CONSOLIDATED INVESTMENT REVIEW

INVESTMENT RECOMMENDATION

INVESTMENT ANALYST

MARKET RESEARCH / COMMERCIAL TEAM

ENGINEERING / TECHNICAL TEAM

LEGAL DEPARTMENT

FINANCE DEPARTMENT

RISK MANAGEMENT

CHIEF INVESTMENT OFFICER

SAP / SYSTEMS

DOCUMENT CONTROLLER

Launch Feasibility Study
RAM-FRM-INV-006

Coordinate Due Diligence Team

Conduct Market Analysis
• Supply & Demand
• Competitor Review
• Occupancy Trends
• Rental Benchmarks
RAM-FRM-INV-007

Perform Technical Due Diligence
• Site Assessment
• Infrastructure Review
• Building Condition Assessment
• Development Constraints
RAM-FRM-INV-008

Review
• Ownership
• Title Deeds
• Encumbrances
• Zoning
• Regulatory Compliance
RAM-FRM-INV-009

Develop Financial Model
• NPV Analysis
• IRR Analysis
• Sensitivity Analysis
• Cash Flow Forecast
• Funding Requirements
RAM-FRM-INV-010

Assess Risks
• Market Risk
• Financial Risk
• Construction Risk
• Legal Risk
• Environmental Risk
RAM-FRM-INV-011

Prepare Consolidated Investment Assessment
RAM-FRM-INV-012

Prepare Investment Recommendation Report
RAM-FRM-INV-013

Review Investment Recommendation Decision Gateway

PROCEED TO INVESTMENT APPROVAL?

Yes

No

Reject / Reassess Opportunity
RAM-FRM-INV-014

Proceed to Phase 3 – Investment Approval

Create Feasibility Project
SAP PS

Financial Analysis Repository
SAP FI/CO

Investment Evaluation Dashboard
SAP Analytics Cloud

Archive Due Diligence Reports
SAP DMS

LEGEND: Start End Process Task Decision Document / Form System / Database Sequence Flow Information Flow

FORMS & TEMPLATES USED (This Phase)

Form Code	Form Name
RAM-FRM-INV-006	Feasibility Study Initiation Form
RAM-FRM-INV-007	Market Assessment Report
RAM-FRM-INV-008	Technical Due Diligence Checklist
RAM-FRM-INV-009	Legal Due Diligence Report
RAM-FRM-INV-010	Financial Feasibility Model
RAM-FRM-INV-011	Risk Assessment Matrix
RAM-FRM-INV-012	Consolidated Investment Assessment
RAM-FRM-INV-013	Investment Recommendation Report
RAM-FRM-INV-014	Investment Approval Submission

KEY PERFORMANCE INDICATORS (KPIs)

- Feasibility Completion Time (Days)
- Due Diligence Completion Rate (%)
- Investment Approval Conversion Rate (%)
- Forecast vs Actual IRR Accuracy (%)
- Risk Identification Effectiveness (%)
- Business Case Acceptance Rate (%)

PROCESS OWNER



Chief Investment Officer

Accountable for end-to-end Feasibility & Due Diligence Process.

SYSTEMS / APPLICATIONS

- SAP RE-FX
- SAP PS
- SAP FI/CO
- SAP GRC
- SAP DMS
- SAP Analytics Cloud
- Power BI

NOTES / OBSERVATIONS

1. No investment may proceed without completed due diligence.
2. Financial models shall include sensitivity scenarios.
3. Legal title verification is mandatory.
4. Risks shall be assessed before recommendation.
5. All reports shall be stored in SAP DMS.
6. Approved opportunities proceed to Phase 3 – Investment Approval.

(All forms are controlled in DMS and available in SAP DMS / SharePoint)

[illegible]

RAM – INVESTMENT & CAPITAL PROJECTS MANAGEMENT PROCESS

PHASE 4 – ACQUISITION & TRANSACTION MANAGEMENT


PPBPMN SWIMLANE DIAGRAM WITH SIPOC

PROCESS PURPOSE:

To execute approved acquisition transactions through negotiation, contract preparation, transaction completion, ownership transfer and asset onboarding into the RAM portfolio.

PROCESS SCOPE:

Applies to all approved acquisitions, joint ventures, strategic investments and property purchases authorized through the Investment Approval Process.

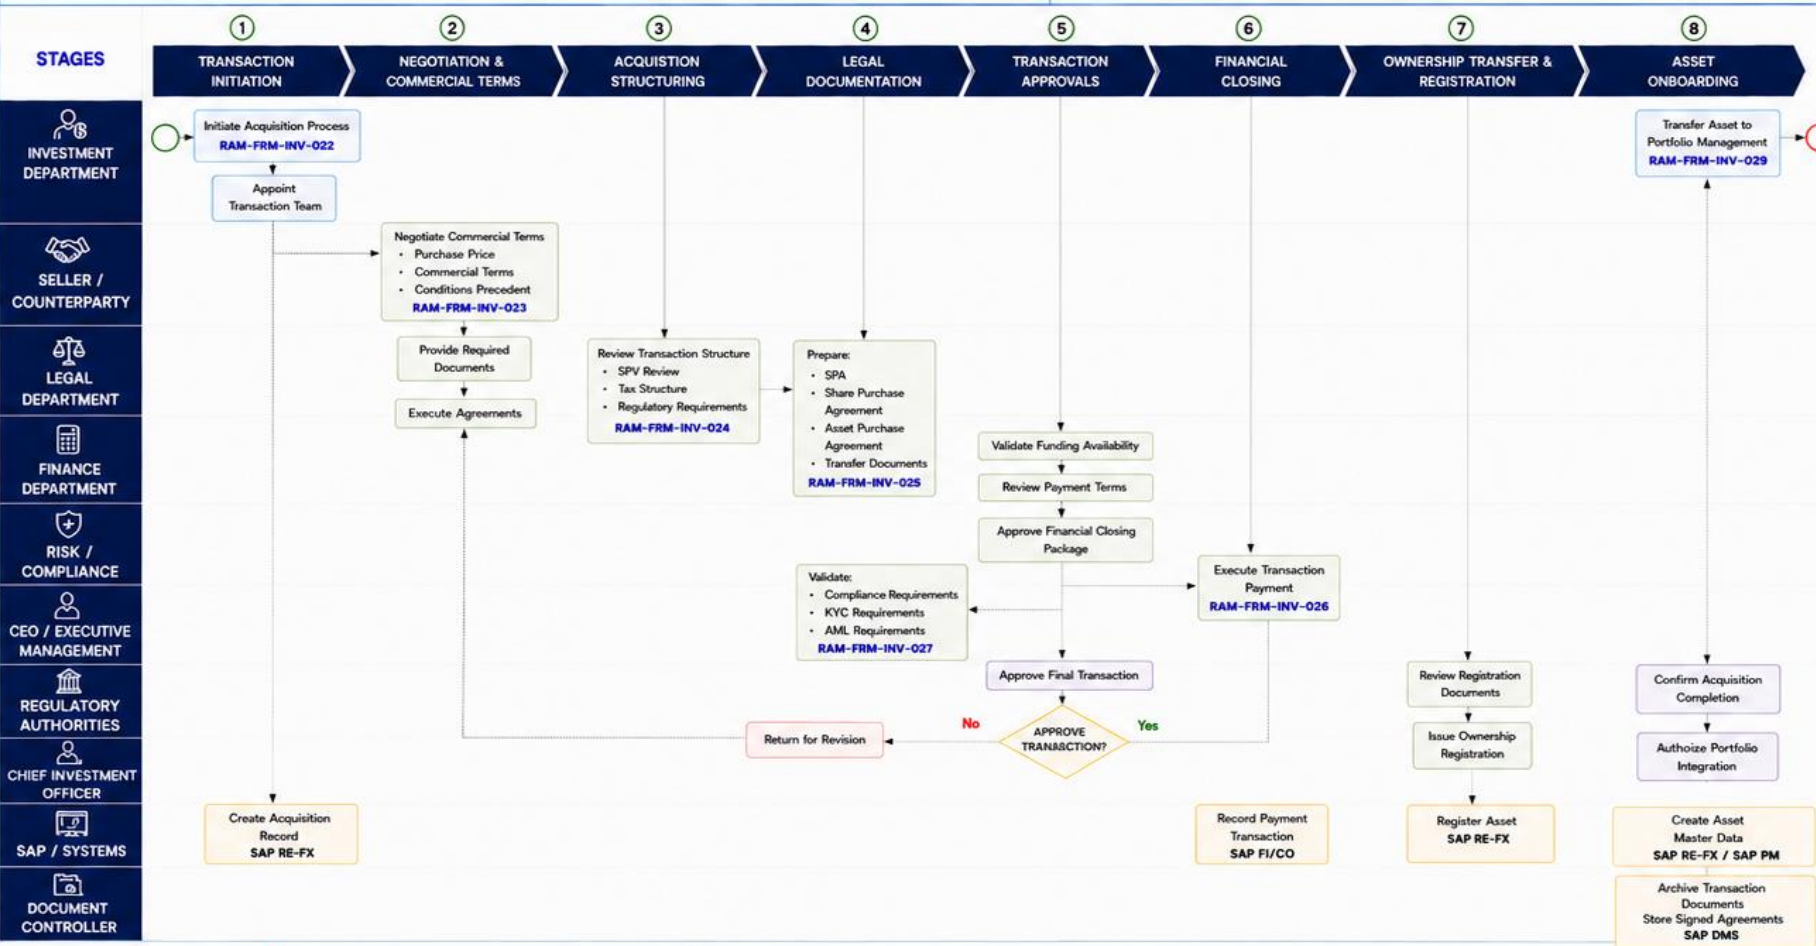

SIPOC

S – SUPPLIERS (Inputs)

- Sellers
- Brokers
- Legal Advisors
- Regulators
- Financial Institutions
- Investment Department

I – INPUTS

- Approved Investment
- Acquisition Strategy
- Due Diligence Reports
- Funding Approval
- Legal Documents
- Transaction Structure

P – PROCESS

- ① Transaction Initiation
- ② Negotiation & Commercial Terms
- ③ Acquisition Structuring
- ④ Legal Documentation
- ⑤ Transaction Approvals
- ⑥ Financial Closing
- ⑦ Ownership Transfer
- ⑧ Asset Onboarding

O – OUTPUTS

- Executed Acquisition Agreement
- Completed Financial Closing
- Registered Ownership
- Asset Master Record
- Portfolio Asset Integration
- Acquisition Completion Report

C – CUSTOMERS

- Board
- CEO
- Portfolio Management
- Asset Management
- Finance
- Operations

LEGEND:

FORMS & TEMPLATES USED (This Phase)		KEY PERFORMANCE INDICATORS (KPIs)	PROCESS OWNER	SYSTEMS / APPLICATIONS	NOTES / OBSERVATIONS
Form Code	Form Name		 Chief Investment Officer Accountable for end-to-end Acquisition & Transaction Management Process.		
RAM-FRM-INV-022	Acquisition Initiation Form	• Acquisition Cycle Time (Days)		• SAP RE-FX	1. No transaction may close without approved funding.
RAM-FRM-INV-023	Negotiation Summary Sheet	• Transaction Success Rate (%)		• SAP FI/CO	2. Legal review is mandatory before execution.
RAM-FRM-INV-024	Transaction Structure Assessment	• Cost Variance (%)		• SAP GRC	3. Ownership registration must be completed immediately after closing.
RAM-FRM-INV-025	Acquisition Agreement Checklist	• Acquisition Completion Rate (%)		• SAP DMS	4. Asset master data shall be created before operational handover.
RAM-FRM-INV-026	Financial Closing Certificate	• Ownership Registration Time (Days)		• CRM	5. All acquisition documents shall be retained in SAP DMS.
RAM-FRM-INV-027	Compliance & KYC Review Form	• Acquisition Budget Compliance (%)		• SharePoint	6. Approved acquisitions proceed to Phase 5 – Development & Capital Projects Management.
RAM-FRM-INV-028	Ownership Registration Form				
RAM-FRM-INV-029	Asset Onboarding Form	• Post-Acquisition Integration Time (Days)			
(All forms are controlled in DMS and available in SAP DMS / SharePoint)					

RAM – INVESTMENT & CAPITAL PROJECTS MANAGEMENT PROCESS

PHASE 5 – DEVELOPMENT & CAPITAL PROJECT EXECUTION


PPBPMN SWIMLANE DIAGRAM WITH SIPOC

PROCESS PURPOSE:

To plan, design, build and deliver capital projects on time, within budget, to quality and safety standards and in alignment with value objectives.

PROCESS SCOPE:

Applies to all capital projects including new developments, major rehabilitations, redevelopments, infrastructure and value-add projects.

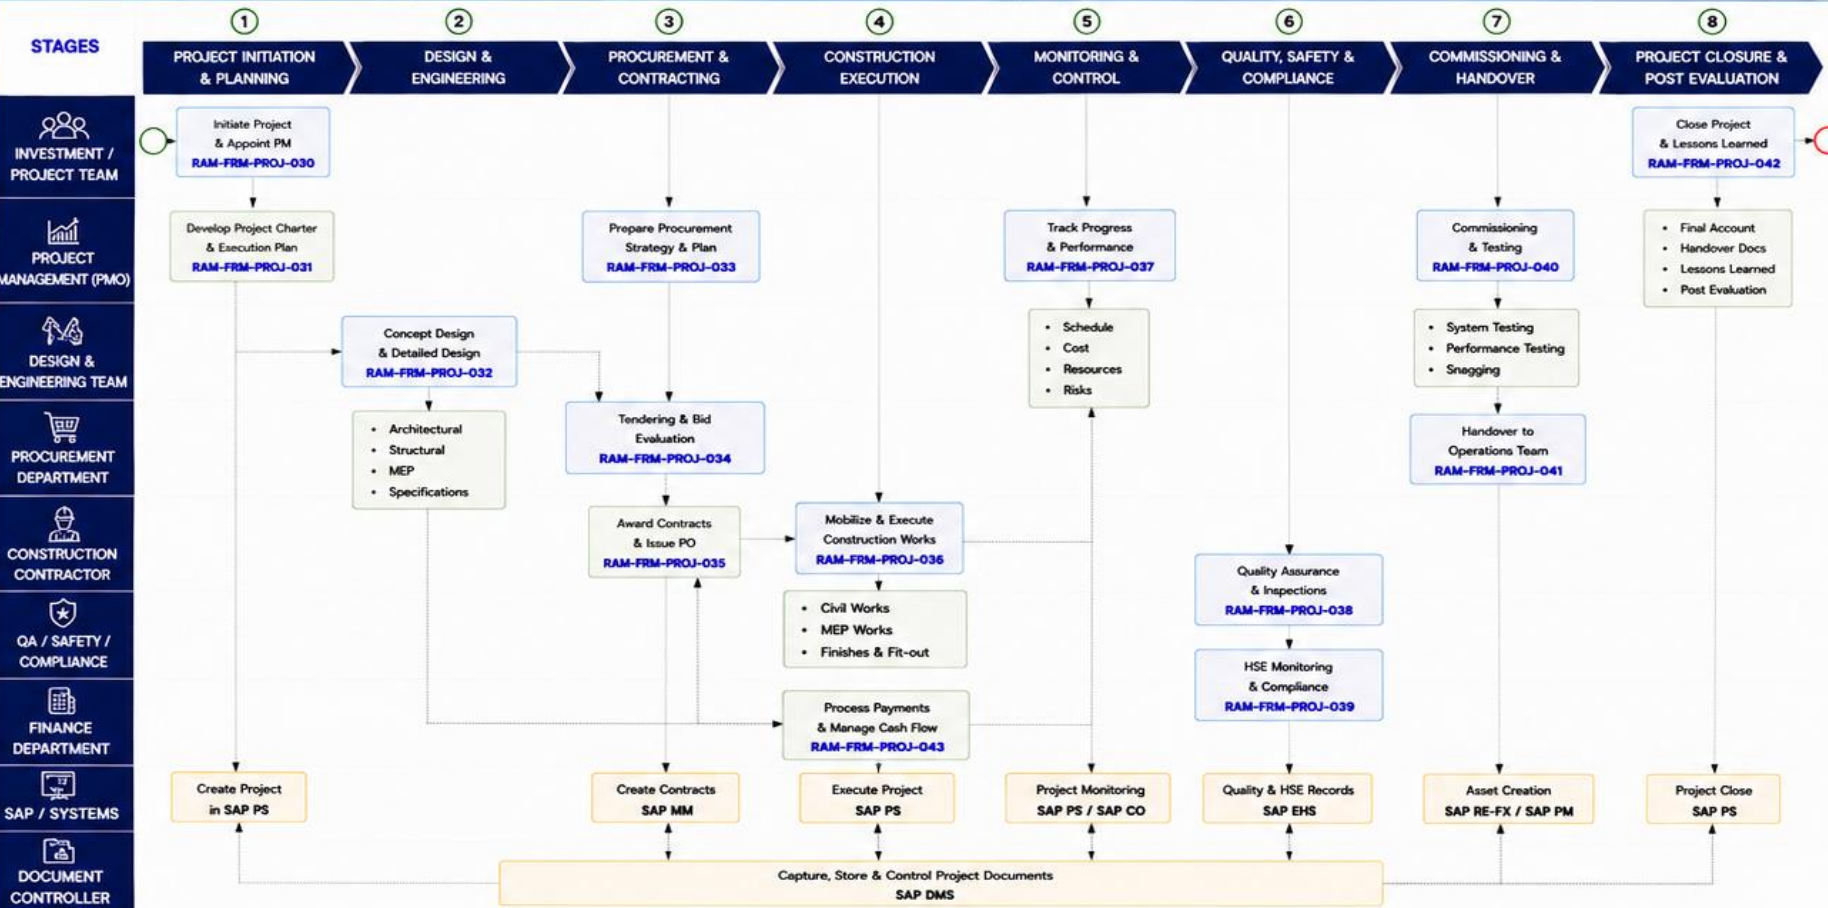

SIPOC

S – SUPPLIERS (Inputs)

- Investment Department
- Design Consultants
- Contractors
- Suppliers
- Regulatory Authorities
- Finance Department

I – INPUTS

- Approved Investment
- Project Scope
- Design Documents
- Contracts
- Budget & Funding
- Regulatory Requirements

P – PROCESS

- Project Initiation & Planning
- Design & Engineering
- Procurement & Contracting
- Construction Execution
- Monitoring & Control
- Quality, Safety & Compliance
- Commissioning & Handover
- Project Closure & Evaluation

O – OUTPUTS

- Completed Project
- Handover Certificate
- Asset Master Record
- Final Accounts
- Project Documentation
- Post Project Evaluation

C – CUSTOMERS

- Board
- CEO
- Asset Management
- Operations
- Finance
- Tenants / End Users

LEGEND: Start (Green circle), End (Red circle), Process Task (Blue box), Decision (Yellow diamond), Document / Form (White box with blue border), System / Database (Blue box with white border), Sequence Flow (Solid arrow), Information Flow (Dashed arrow)

FORMS & TEMPLATES USED (This Phase)		KEY PERFORMANCE INDICATORS (KPIs)	PROCESS OWNER	SYSTEMS / APPLICATIONS	NOTES / OBSERVATIONS
Form Code	Form Name				
RAM-FRM-PROJ-030	Project Initiation Form	- Schedule Performance Index (SPI) - Cost Performance Index (CPI) - Budget Variance (%) - Project Completion Rate (%) - Quality Compliance Rate (%) - Safety Incident Rate (LTIFR) - Change Order Variance (%) - On-Time Project Delivery (%) - Project ROI Achievement (%) - Post Project Satisfaction (%)	 Chief Investment Officer Accountable for end-to-end Development & Capital Projects Execution Process.	- SAP PS - SAP MM - SAP FI/CO - SAP PM - SAP EHS - SAP RE-FX - SAP DMS - Power BI / SAP Analytics Cloud	- Projects shall be executed in line with approved scope, time, cost and quality standards. - All changes shall follow the Change Management Process. - Safety and compliance are mandatory throughout execution. - Asset creation in SAP shall occur before operational handover. - All project documents shall be archived in SAP DMS. - Completed projects proceed to Phase 6 – Operations & Asset Performance Management.
RAM-FRM-PROJ-031	Project Charter				
RAM-FRM-PROJ-032	Design & Engineering Report				
RAM-FRM-PROJ-033	Procurement Plan				
RAM-FRM-PROJ-034	Bid Evaluation Report				
RAM-FRM-PROJ-035	Contract Award Form				
RAM-FRM-PROJ-036	Construction Execution Plan				
RAM-FRM-PROJ-037	Progress Report				
RAM-FRM-PROJ-038	QA Inspection Report				
RAM-FRM-PROJ-039	HSE Compliance Report				
RAM-FRM-PROJ-040	Commissioning Report				
RAM-FRM-PROJ-041	Handover Certificate				
RAM-FRM-PROJ-042	Project Closure Report				
RAM-FRM-PROJ-043	Payment Certificate				

(All forms are controlled in DMS and available in SAP DMS / SharePoint)

RAM – INVESTMENT & CAPITAL PROJECTS MANAGEMENT PROCESS

PHASE 6 – ASSET COMMISSIONING & HANDOVER

PPBPMN SWIMLANE DIAGRAM WITH SIPOC

PROCESS PURPOSE:

To ensure completed projects and developments are tested, commissioned, and formally handed over to operations, with all documentation, compliance, and asset information complete and accurate.

PROCESS SCOPE:

Applies to all completed capital projects and developments prior to operational handover and integration into the asset management lifecycle.

SIPOC

S – SUPPLIERS (Inputs)

- Project Management Team
- Contractors
- Design Consultants
- Quality & HSE Department
- Operations Team
- Finance Department

I – INPUTS

- Completed Project
- As-Built Drawings
- Test Reports
- O&M Manuals
- Compliance Certificates
- Warranties

P – PROCESS

- ① Commissioning Planning
- ② Systems & Equipment Testing
- ③ Quality & Compliance Verification
- ④ Documentation Completion
- ⑤ Operational Readiness
- ⑥ Final Handover Approval
- ⑦ Asset Registration & Activation
- ⑧ Post-Handover Review

O – OUTPUTS

- Commissioning Completion Certificate
- Handover Certificate
- Asset Master Record
- O&M Documentation
- Operational Asset
- Post-Handover Report

C – CUSTOMERS

- Operations Department
- Asset Management
- Finance Department
- Board / Management
- Tenants / Customers

STAGES

①

②

③

④

⑤

⑥

⑦

⑧

COMMISSIONING PLANNING

SYSTEMS & EQUIPMENT TESTING

QUALITY & COMPLIANCE VERIFICATION

DOCUMENTATION COMPLETION

OPERATIONAL READINESS

FINAL HANDOVER APPROVAL

ASSET REGISTRATION & ACTIVATION

POST-HANDOVER REVIEW

PROJECT MANAGEMENT TEAM

DESIGN & CONSULTANTS

CONTRACTOR

QUALITY & HSE DEPARTMENT


OPERATIONS TEAM

FINANCE DEPARTMENT

CHIEF INVESTMENT OFFICER

SAP / SYSTEMS

DOCUMENT CONTROLLER

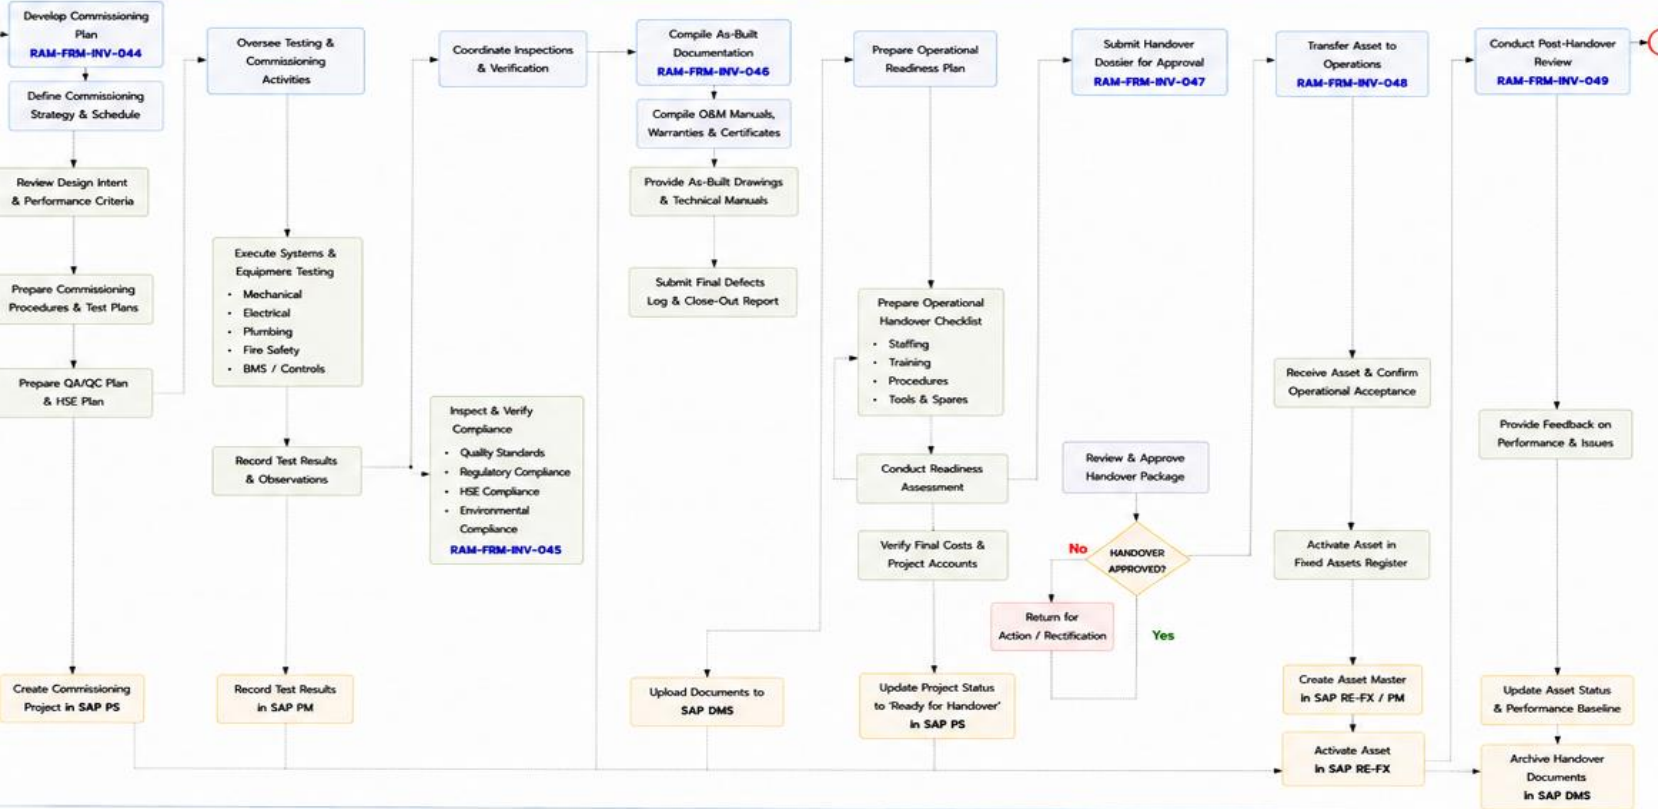

LEGEND: Start End Process Task Decision Document / Form System / Database Sequence Flow Information Flow

FORMS & TEMPLATES USED (This Phase)

KEY PERFORMANCE INDICATORS (KPIs)

PROCESS OWNER

SYSTEMS / APPLICATIONS

NOTES / OBSERVATIONS

Form Code	Form Name
RAM-FRM-INV-044	Commissioning Plan
RAM-FRM-INV-045	Compliance Verification Report
RAM-FRM-INV-046	As-Built Documentation Checklist
RAM-FRM-INV-047	Handover Approval Submission
RAM-FRM-INV-048	Asset Handover Certificate
RAM-FRM-INV-049	Post-Handover Review Report

- Commissioning Completion Rate (%)
- Handover on Schedule (% of Projects)
- Defects Closed Before Handover (%)
- Handover Approval Cycle Time (Days)
- Documentation Accuracy Rate (%)
- Asset Activation Timeliness (Days)
- Post-Handover Issue Resolution Rate (%)



Chief Investment Officer

Accountable for end-to-end Asset Commissioning & Handover Process.

- SAP PS
- SAP PM
- SAP RE-FX
- SAP FI/CO
- SAP DMS
- SAP GRC
- SAP Analytics Cloud
- Power BI

1. No operational handover without all tests and certifications complete.
2. All defects must be closed before final approval.
3. As-built documentation must be accurate and complete.
4. Asset master must be created before operations takeover.
5. Post-handover review ensures continuous improvement.
6. Completed assets proceed to Phase 7 – Asset & Portfolio Management.

(All forms are controlled in DMS and available in SAP DMS / SharePoint)

PPBPMN SWIMLANE DIAGRAM WITH SIPOC

FORMS & TEMPLATES USED (This Phase)		KEY PERFORMANCE INDICATORS (KPIs)	PROCESS OWNER	SYSTEMS / APPLICATIONS	NOTES / OBSERVATIONS
Form Code RAM-FRM-INV-050 RAM-FRM-INV-051 RAM-FRM-INV-052 RAM-FRM-INV-053 RAM-FRM-INV-054 RAM-FRM-INV-055 RAM-FRM-INV-056 RAM-FRM-INV-057 RAM-FRM-INV-058	Form Name Asset Management Plan Asset Performance Scorecard Leasing Strategy Form Annual Budget & Forecast Form Compliance Monitoring Form Portfolio Optimization Form Capital Expenditure Request Value Enhancement Proposal Asset Performance Report	• Occupancy Rate (%) • Net Operating Income (NOI) Growth (%) • Portfolio Yield (%) • Operating Expense Ratio (%) • Tenant Retention Rate (%) • Capital Expenditure Compliance (%) • Maintenance Compliance (%) • Portfolio IRR (%) • Asset Performance Index (API) • Total Portfolio Value Growth (%)	Chief Investment Officer Accountable for end-to-end Asset & Portfolio Management Process.	• SAP RE-FX • SAP FI/CO • SAP PM • SAP GRC • SAP Analytics Cloud • Power BI • SAP DMS • CRM	1. Regular performance monitoring ensures value creation. 2. Maintenance compliance improves asset longevity. 3. Leasing strategy maximizes income and tenant quality. 4. Risks must be identified and mitigated proactively. 5. Portfolio optimization ensures best use of capital. 6. Accurate reporting supports investor confidence. 7. Optimized assets proceed to continuous management cycle and may be considered for exit or redevelopment.

RAM – INVESTMENT & CAPITAL PROJECTS MANAGEMENT PROCESS

PHASE 8 – DIVESTMENT & EXIT MANAGEMENT


PPBPMN SWIMLANE DIAGRAM WITH SIPOC

PROCESS PURPOSE:

To execute value-maximizing divestment and exit strategies for assets at the right time and under the right conditions to achieve investment objectives and generate returns.

PROCESS SCOPE:

Applies to all assets and investments within the RAM portfolio that are identified for divestment or exit.

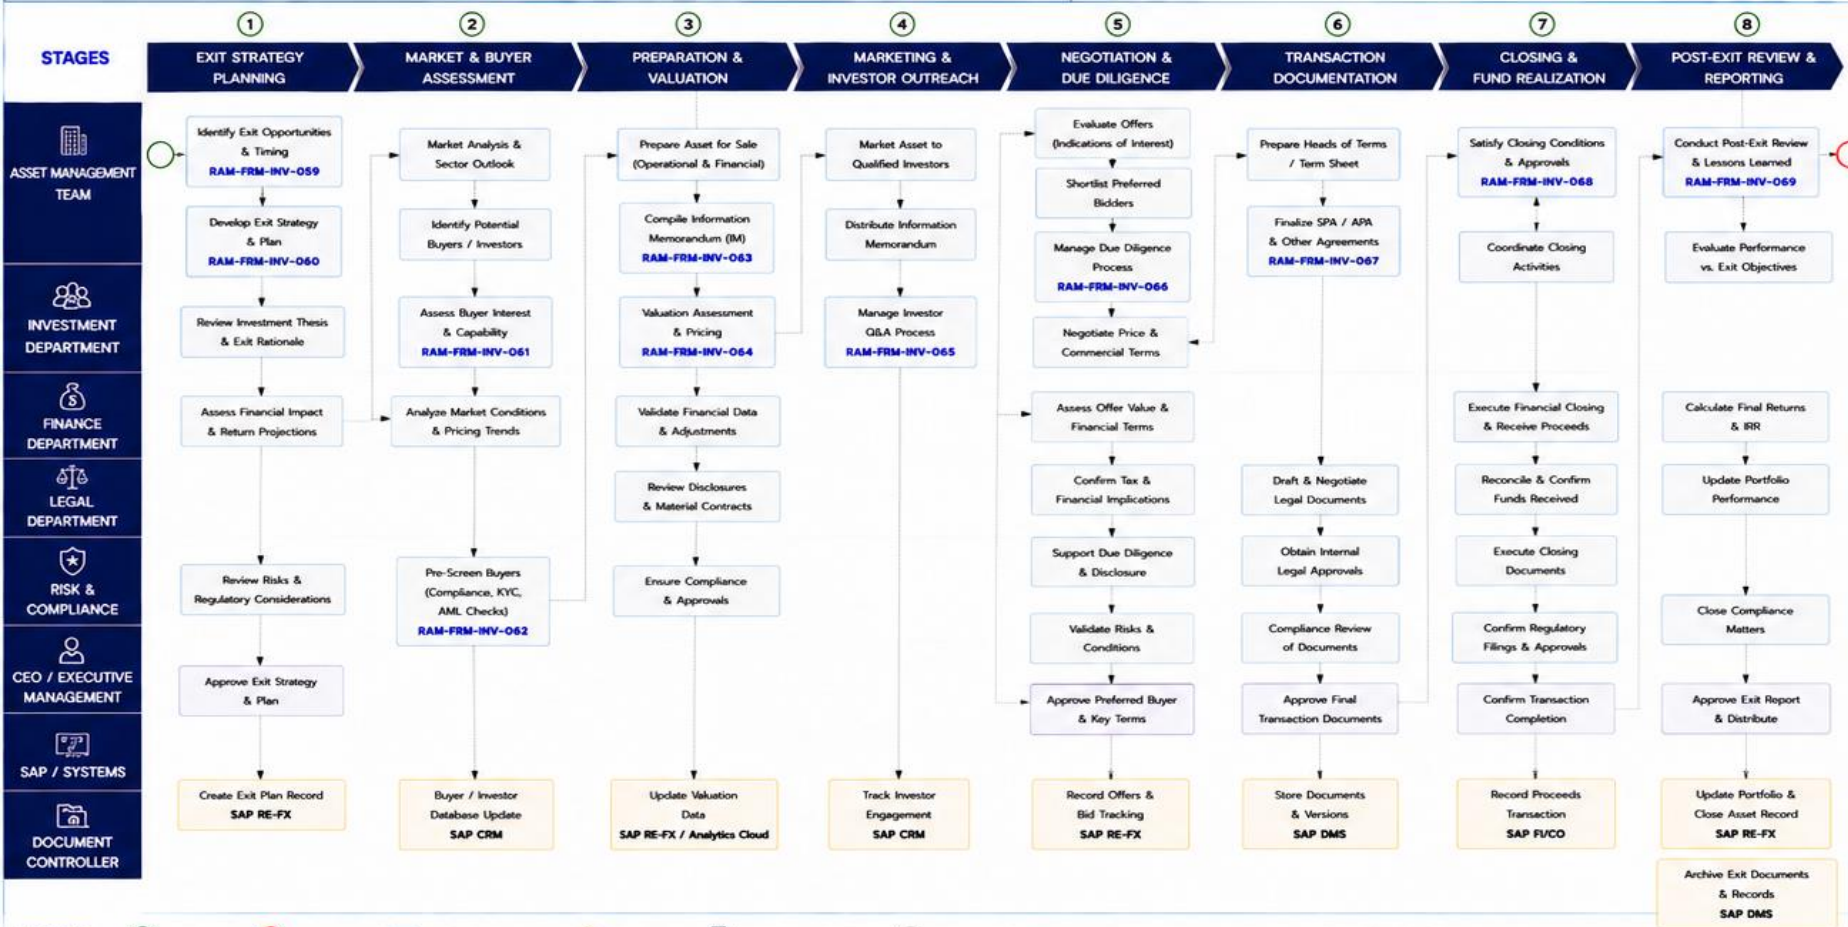

SIPOC

S – SUPPLIERS (Inputs)

- Asset Management Team
- Investment Department
- Finance Department
- Legal Department
- Risk & Compliance
- External Advisors
- Market Participants

I – INPUTS

- Portfolio Assets
- Exit Strategy & Plan
- Financial Information
- Market Data
- Asset Valuations
- Legal Agreements
- Regulatory Requirements

P – PROCESS

- Exit Strategy Planning
- Market & Buyer Assessment
- Preparation & Valuation
- Marketing & Outreach
- Negotiation & Due Diligence
- Transaction Documentation
- Closing & Fund Realization
- Post-Exit Review & Reporting

O – OUTPUTS

- Executed Exit Transaction
- Cash Proceeds Realized
- Final Investment Returns
- Updated Portfolio Records
- Exit Performance Report
- Lessons Learned Report

C – CUSTOMERS

- Board
- Investors
- CEO
- Finance Department
- Asset Management
- Stakeholders

FORMS & TEMPLATES USED (This Phase)

Form Code	Form Name
RAM-FRM-INV-059	Exit Opportunity Assessment
RAM-FRM-INV-060	Exit Strategy Plan
RAM-FRM-INV-061	Buyer Assessment Report
RAM-FRM-INV-062	Buyer Due Diligence Checklist
RAM-FRM-INV-063	Information Memorandum Template
RAM-FRM-INV-064	Valuation Summary Report
RAM-FRM-INV-065	Investor Engagement Log
RAM-FRM-INV-066	Due Diligence Tracking Sheet
RAM-FRM-INV-067	Transaction Document Checklist
RAM-FRM-INV-068	Closing Checklist
RAM-FRM-INV-069	Post-Exit Review Report

(All forms are controlled in DMS and available in SAP DMS / SharePoint)

KEY PERFORMANCE INDICATORS (KPIs)

- Exit Cycle Time (Days)
- Exit IRR (% vs Plan)
- Exit Price vs Valuation (%)
- Total Proceeds Realized (AED)
- Exit Success Rate (%)
- Portfolio Realization Rate (%)
- Cash-on-Cash Return (%)
- Exit Cost as % of Proceeds (%)
- Post-Exit Issue Resolution Time (Days)

PROCESS OWNER



Chief Investment Officer

Accountable for end-to-end
Divestment & Exit
Management Process.

SYSTEMS / APPLICATIONS

- SAP RE-FX
- SAP FI/CO
- SAP DMS
- SAP GRC
- SAP Analytics Cloud
- SAP CRM
- Power BI

NOTES / OBSERVATIONS

- Exits must align with RAM investment objectives and market conditions.
- All regulatory and tax obligations must be satisfied before closing.
- Complete and accurate information must be provided to buyers.
- Proceeds must be recorded and reconciled in SAP FI/CO.
- Lessons learned must feed back into investment decision framework.
- Completed exits feed into capital recycling for new investments.
- Closed assets proceed to Portfolio Archive in SAP RE-FX.

NOTES

- Notes

- [illegible]
